

ALLOWANCE AUTHORIZATION FORM

Project Name: Courthouse Covered Entryway at the Baldwin County Courthouse

Name of Allowance Account: Owner's Allowance

Authorization No.: 6

Date: 10-07-25

In accordance with Specification Section 0101 - "BASE BID, ALTERNATES & ALLOWANCES", the Contractor, Tindle Construction, LLC, is hereby authorized to proceed with the changes in Work as are described below and is to be paid for the performance of these changes as provided in Specification Section 0101. This Authorization shall become effective when it is signed by the Contractor and the Owner's Representative, and it is understood and agreed that the amount(s) stipulated below constitute full compensation for these changes in Work.

Description of the Work under this Authorization: Install riser at storm sewer. See attached.

Total amount of this Authorization: (\$3,450.00)

Original amount of the Allowance:	\$150,000.00
Net total of Previous Authorizations:	(\$50,537.28)
Previous Remaining Allowance:	\$99,462.72
Total amount of this Authorization:	(\$3,450.00)

Allowance Remaining after this Authorization \$96,012.72

Recommended by:

Authorized by:

Accepted by:



ARCHITECT

CITY/COUNT/STATE AGENCY



Contractor

Tindle Construction

General Contracting

DATE: 10/2/2025

CONTRACTOR NAME: Tindle Construction, LLC

PROJECT NAME: Courthouse Covered Entry Project

GC JOB NUMBER: 2302GV

REFERENCE CHANGE OF PROPOSAL REQUEST NUMBER: 6

ARCHITECT NAME:
PH&J

INITIATED BY:
OWNER/ARCHITECT
GC
SUBCONTRACTOR

BRIEF DESCRIPTION OF PROPOSED CHANGE:

Rise for drainage. See attached.

ITEM DESCRIPTION	QUANTITY	UNIT COST	SUBCONTRACTOR	MAN HOURS	HOURLY RATE	LABOR	EQUIPMENT
Delta Saurth	1	3450	\$3,450.00				\$0.00
			\$0.00				\$0.00
			\$0.00				\$0.00
			\$0.00				\$0.00
			\$0.00				\$0.00
			\$0.00				\$0.00
			\$0.00				\$0.00
			\$0.00				\$0.00

SUBCONTRACTOR:	\$3,450.00
LABOR:	\$0.00
EQUIPMENT:	\$0.00
SUBTOTAL: (DIRECT COST)	\$3,450.00
OVERHEAD&PROFIT:	\$ -
SALES/USE TAX:	\$0.00
TOTAL COST CHANGE:	\$3,450.00

ADD DEDUCT x



Change Order

Delta South Contracting
PO Box 131
Churchula, AL 36521

Contractor:
Tindle Construction
3456 Halls Mill Road
Mobile, AL 36693

Date: 10/2/2025

Project: Baldwin County Courthouse

Contract No: _____

ATTN: Austin Bosarge

Change Order No: 2

This change order modifies the contract as described below. Unless expressly modified by this change order, the terms and condition of the contract remain in full force and effect and apply to the modification required by this change order.

The following is additional/deleted item(s) to your contract:

PRICE

- | | |
|---|-------------|
| 1. Core Drill existing approved drainage box for 15" rcp on the south side of the box | \$ 250.00 |
| 2. Installation of a riser system between the drainage box and lid. | \$ 3,200.00 |

Change Order Price Total: \$ 3,450.00

This change order has no effect on the completion date(s)/delivery due date(s) required by the contract unless expressly stated to the contrary in this change order.

The total adjustment of the contract price for this change order is a addition of **\$3,450.00** to the original, or previously adjusted, price of **\$99,250.00**, thereby making the total price at this date the sum of **\$ 102,700.00**

PLEASE SIGN AND RETURN ONE COPY TO THE ABOVE ADDRESS WITHIN 10 CALENDAR DAYS

DELTA SOUTH CONTRACTING

Accepted By: _____
Title: _____
Company Name: _____
Date: _____

By: _____
James Bradley
Title: Project Manager

Job Name: Baldwin County Courthouse
 Contractor: Delta South Contracting
 Job Location: Baldwin

Submittal/Shop
 251-653-1399

- Concrete: 4000 psi, Type 1/II Cement
- Reinforcement per ASTM C-913 (Square)
- Reinforcement per ASTM C-478 (Round)

9/30/2025

Structure ID: **BCC-1**
 Spec: Alabama
 Type: Storm JB-MH SL
 Size: 48"

Rim: 271.17'
 Invert: 262.87'
 Rim to Invert: 8.3'

Overall Height: 9.25'
 Sump: 3.5"
 Floor (Top): 262.578'


Structure Notes:
 Verify Invert Prior To Construction




1) 24" - EJ-1337OT - STD - 6"	251 lb
1) 48" - Flat Lid EC24 - 8"	1521 lb
1) 48" - MH Riser - 12"	867 lb
1) 48" - MH Riser - 48"	3469 lb
1) 48" - MH Base INC SW - 29"	3590 lb
2) 22" - Round	0 lb
Structure Total:	9698 lb

Position	Elev	Angle	Pipe	Connector	Up ()
Rim	271.17'				
Reducer					
Invert 1	262.87'	0°	15" RCP-Round	22" Round	0"
Invert 2	262.87'	180°	15" RCP-Round	22" Round	0"
Invert 3					
Invert 4					
Invert 5					
Invert 6					

PLAN




INVERTED



48" - MH Base INC SW - 29"

PROFILE

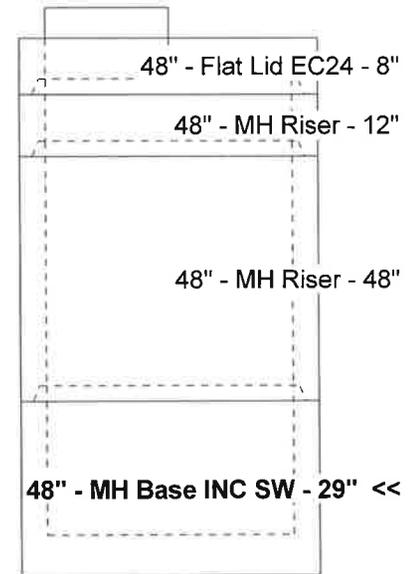

Job Name: Baldwin County Courthouse
Contractor: Delta South Contracting
Job Location: Baldwin

Submittal/Shop: 251-653-1399

1. Concrete: 4000 psi, Type 1/II Cement
 2. Reinforcement per ASTM C-913 (Square)
 3. Reinforcement per ASTM C-478 (Round)

9/30/2025 Page: 2 of 3

Structure ID: BCC-1
Spec: Alabama
Type: Storm JB-MH SL
Size: 48"

Rim: 271.17'
Invert: 262.87'
Rim to Invert: 8.3'




Overall Height: 9.25'
Sump: 3.5"
Floor (Top): 262.578'

Structure Notes:
 Verify Invert Prior To Construction



1) 24" - EJ-1337OT - STD - 6"	251 lb
1) 48" - Flat Lid EC24 - 8"	1521 lb
1) 48" - MH Riser - 12"	867 lb
1) 48" - MH Riser - 48"	3469 lb
1) 48" - MH Base INC SW - 29"	3590 lb
2) 22" - Round	0 lb
Structure Total:	9698 lb

Position	Elev	Angle	Pipe	Connector	Up ()
Rim	271.17'				
Reducer					
Invert 1	262.87'	0°	15" RCP-Round	22" Round	0"
Invert 2	262.87'	180°	15" RCP-Round	22" Round	0"
Invert 3					
Invert 4					
Invert 5					
Invert 6					

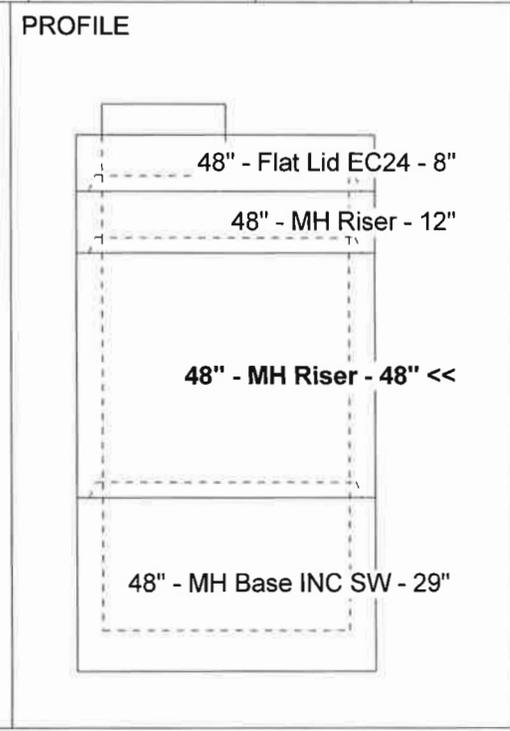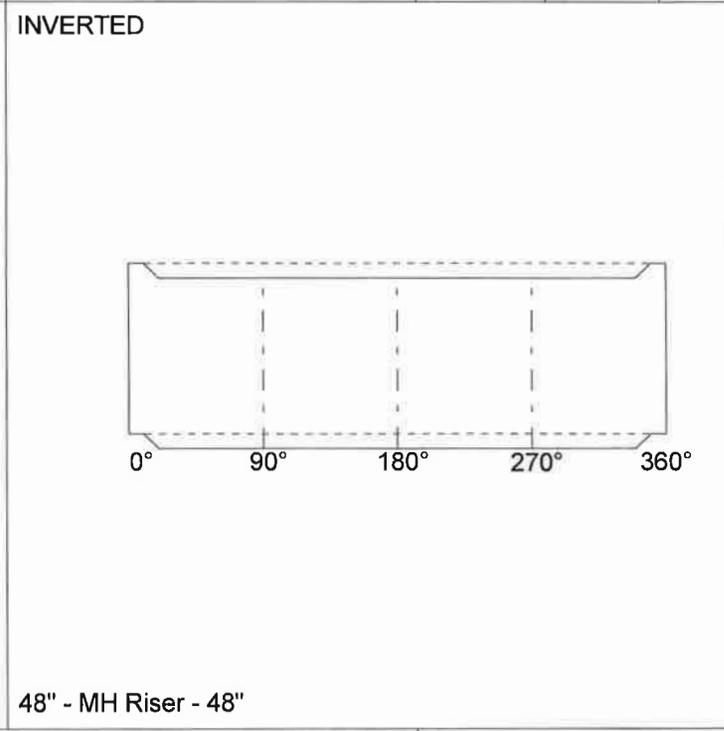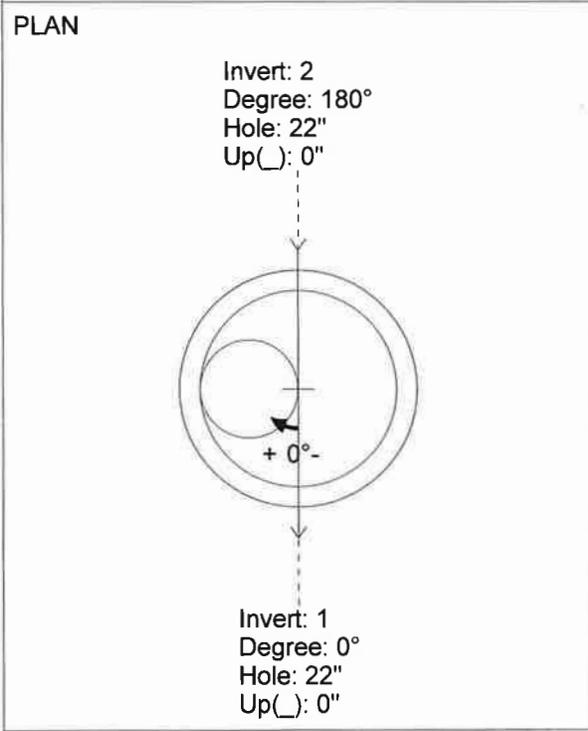

Job Name: Baldwin County Courthouse
Contractor: Delta South Contracting
Job Location: Baldwin

Submittal/Shop
 251-653-1399

1. Concrete: 4000 psi, Type 1/II Cement
 2. Reinforcement per ASTM C-913 (Square)
 3. Reinforcement per ASTM C-478 (Round)

9/30/2025
 Page: 3 of 3

Structure ID: BCC-1
Spec: Alabama
Type: Storm JB-MH SL
Size: 48"

Rim: 271.17'
 Invert: 262.87'
 Rim to Invert: 8.3'

Overall Height: 9.25'
Sump: 3.5"
Floor (Top): 262.578'

Structure Notes:
 Verify Invert Prior To Construction



1) 24" - EJ-1337OT - STD - 6"	251 lb
1) 48" - Flat Lid EC24 - 8"	1521 lb
1) 48" - MH Riser - 12"	867 lb
1) 48" - MH Riser - 48"	3469 lb
1) 48" - MH Base INC SW - 29"	3590 lb
2) 22" - Round	0 lb
Structure Total:	9698 lb

Position	Elev	Angle	Pipe	Connector	Up ()
Rim	271.17'				
Reducer					
Invert 1	262.87'	0°	15" RCP-Round	22" Round	0"
Invert 2	262.87'	180°	15" RCP-Round	22" Round	0"
Invert 3					
Invert 4					
Invert 5					
Invert 6					

